

STATEMENT OF WORK – (Sonrava Health – Customer Service)

This Statement of Work (“SOW”) dated September 30, 2024, is between **XYZ(UK)** (“XYZ”) and **ABC** (“Client” or “”) pursuant to and is subject to the terms of the Master Services Agreement (“Agreement”) entered as of December 15, 2023. All terms capitalized but not defined in this SOW shall have the same meaning as defined under the Agreement.

This SOW is divided into the following sections:

A. PROJECT NAME:

- Customer Service for Dental Appointments

B. SOW TERM: The term of this SOW shall commence on the Effective Date and shall be valid for a period of five (5) years (“Term”). In accordance with Section 3 of the Agreement, Client may terminate this SOW (in whole or in part) at any time without cause, including for convenience, upon one hundred twenty (120) days’ prior written notice to XYZ.

The parties may extend the Term of this SOW by mutual agreement by executing a written amendment to this SOW.

C. DESCRIPTION OF SERVICES, SCOPE, & DELIVERABLES: The Client and XYZ have mutually agreed to engage Services with one (1) service line. All in-scope service lines will be treated as separate work types with separate metrics.

- a. Inbound - The XYZ team shall answer inbound calls related to new patient dental service appointments.

D. Scope of Services as listed below:

a. Inbound Calls

i. In-Scope:

1. Skill Set – Voice
2. To answer inbound calls for new patient dental service appointments

ii. Client Applications

1. VDI – Virtual Desktop Infrastructure
2. Denticon Patient Window
3. Call Center Tool – New Patient Routing
4. Atlas for Office Addresses
5. Call Center ECHAT / CCA Team
6. Genesys Telephony

iii. Activities



1. Scheduling new appointments
2. Rescheduling existing appointments
3. Handling appointment cancelations

iv. Out-of-Scope:

1. Spanish-speaking LOB. This scope may get addressed via a separate change order in due course.
2. Outbound Line of Business (LOB): The XYZ team is only responsible for making outbound calls to patients who missed their dental service appointments when there is no inbound call volume and outbound calls for year-end campaigns.

FTEs Split:

Production headcount: The overall expected scope shall be for 175 FTEs for customer service (English) spread between an initial wave of 25 FTEs, followed by a 150 FTE ramp up immediately thereafter.

Sonrava shall have full discretion to increase or decrease the total FTE count on this project upon notice to XYZ, which shall be subject to locked forecast provided by Client to XYZ as stated in Section E (m) "Shift Window". Notwithstanding the foregoing, Client has the discretion to modify the FTE count in accordance with the following tiers:

- 30 days' notice for FTE headcount modifications of 10 or fewer;
- 60 days' notice for FTE headcount modifications of 11 to 25;
- 90 days' notice for FTE headcount modifications of 26 to 35.
- NOTWITHSTANDING ANYTHING CONTRARY IN THIS SOW, the reduction of FTE (Ramp down) by 20% or more in aggregate within six (6) months or 40% or more within one (1) year shall be deemed partial termination for without cause and subject to one twenty (120) days' notice for such termination, as per the section 3 of the Agreement.

Any change in the headcount will be executed through a Change Order to ensure that the Parties make the adjustments in a structured manner. This approach provides flexibility while maintaining the quality and effectiveness of the Service delivery.

E. Project Services Terms & Conditions:

As of the Effective Date and during the Term, the parties agree to the following terms and conditions:

- a. Client shall provide an electronic training manual to XYZ, including Client's sample claim cases and reports, describing the workflow process, protocols, guidelines, report requirements, forms, templates, and any other information Client deems reasonably necessary for the Services.



b. Client personnel shall train XYZ personnel on the Client’s software and systems as the Client, in its sole discretion, deems reasonably required for the Services. The Client will complete the onboarding training per the timelines in the table below.

Strategy	Type	Approach	Mode	Process Training Dates**
Inbound	Client Trainer to XYZ Pilot Staff	Train The Batch	Face to Face	September 30, 2024 – October 14, 2024

** Subject to: Timely access to applications and all other mandatory requirements completed on time.

c. Client and XYZ agree to provide additional software as deemed necessary by mutual agreement of the parties to the Services. The Client grants XYZ a fully paid –up license to access and use the Client’s software only to the extent necessary for the sole purpose of providing the Services under this SOW.

d. Neither Client nor XYZ will supply or bear the cost of any IT hardware equipment to the other for the Services. XYZ agrees to provide the equipment necessary for it to perform the Services at its own expense.

e. Solely for the performance of the Services, Client will provide XYZ with direct access to Client’s systems and software twenty-four (24) hours per day, seven days a week, except for during scheduled maintenance (with at least twenty-four (24) hour advance notice) and U.S. holidays. The client agrees to provide such access by assigning login credentials to relevant XYZ production resources; team leads quality assurance, trainers, supervisors, and management. XYZ shall use its access to the Client's systems and software solely and exclusively to provide Services as set forth in this SOW and for no other purposes.

f. If Client’s systems or software is not accessible by XYZ due to system issues caused by Sonrava during XYZ’s normal hours of operation (“Downtime”), the applicable Turnaround Time requirement, wherever applicable, shall be adjusted proportionately and only to the extent of the actual Downtime. Any Downtime hours and the impact on applicable TAT requirements, wherever applicable, will be mutually agreed upon by appropriate representatives of Client and XYZ.

g. Client and XYZ agree to work jointly and collaboratively during the Term to implement the Services, including reasonable access to Client’s facilities, data, computer and storage systems, and personnel, as may reasonably be required for the implementation and installation of equipment, software, or connectivity, and the development of Services including Report formats, systems, protocols, training, enhancements, and the efficient and economical transfer of information.

h. Client will provide XYZ with information, data, content, forms, and templates deemed necessary by Client for the Services and as reasonably requested by XYZ. Client agrees to provide



IT staffing resources it determines to be reasonably necessary to develop and implement procedures for the Services.

- i. Client and XYZ will each designate a project manager for the Services and provide the other with that person’s contact information. In the event of a change, the parties will give notice of the change as soon as practicable and identify the replacement project manager.
- j. XYZ shall provide sufficient staffing levels to deliver the Services, based on the projected monthly baseline volume. Client will provide XYZ a minimum of ninety (90) days’ notice for any material increase or decrease in the projected monthly baseline volume.
- k. XYZ agrees to provide appropriate Quality Control (“QC”) for the duration of the Services. Client and XYZ shall jointly develop and mutually agree upon an audit plan with sampling strategy for each service line and have a detailed quality standard document in place to govern quality assurance.
- l. Client will provide XYZ with any changes to its protocols or guidelines as soon as practicable and XYZ shall implement such protocols or guidelines within ten (10) business days, or as otherwise mutually agreed by Client and XYZ. In its sole discretion, Client agrees to train XYZ resources for any training required to implement Service changes. The changes to scheduling shall be added to SharePoint and XYZ will have access, updates will be posted in WFM Teams Chat.
- m. **Shift Window** - XYZ will provide the Services 9 hours per day, Monday through Sunday (other than on Client holidays) and will make its QC staff available during such time.

Proposed Hours of operations for each Service Line are described in the table below:

Process	Time Zone	Shift Time	Days
Inbound	Eastern Standard Time	24/7	Monday – Sunday

*90 day locked forecasted volume will be shared by the client 1 month in advance

- n. XYZ will report a type and frequency as mutually agreed by the parties, including XYZ QA results and key performance metrics. The client will provide system-generated reports for this process to calculate mutually agreed critical to process metrics like TAT, Productivity, etc., for each work queue or work list across all 3 Service lines. Additionally, XYZ will provide routine updates to Client of progress, issues and decisions needed to ensure continuity of work quality and performance. Issues lists and decisions will be maintained by XYZ and updated mutually.
- o. Client agrees to provide XYZ with documented quality references and guidelines on which it intends to base XYZ QC oversight review and determination of XYZ performance, including scoring of calls by the Client’s Quality Assurance Department. Client agrees to provide QA



feedback as per the quality standard document, which may be updated by Client and XYZ from time to time, during the period of the Services.

- p. Any material or system application-related changes affecting the Services during the contract term will be communicated to XYZ with minimum 30 (thirty) days’ notice.
- q. **Implementation Plan** – Initial 180 days from the BAU Go Live Date will be treated as baselining period to measure actual performance against the Service targets.

The BAU Go-live dates (post completion of ramp up period) for the following Service lines are stated below (“BAU Go Live/ BAU Go Live Date”):

- I. Wave 1 WDS – November 18, 2024
- II. Wave 2 WDS – December 16, 2024
- III. Wave 3 MADP – December 16, 2024
- IV. Wave 3 PURE – December 23, 2024
- V. Wave 4 MADP/WDS – December 23, 2024


- r. **Delivery Location** – XYZ will provide services from the Philippines.
- s. **Governance Framework—The** Client and XYZ will jointly work towards making the agreement a success. To monitor progress, a robust governance framework will be implemented, as outlined in the table below. The structure below may be altered at any time during the Term as agreed upon by the appropriate Client and XYZ personnel.
 - I. **Weekly Performance Review**—Identified resources from the Client and XYZ will meet to discuss XYZ's performance for the previous week, challenges, and help items. Performance meeting bi-weekly or as needed to support changes.
 - II. **Monthly Business Review—The** Client and XYZ management teams will meet once a month to discuss XYZ's performance for the previous month and to brainstorm process improvement ideas for the following months.

Project Service	Structure	Purpose
Inbound	1. Weekly performance review with identified Client managers for 30 minutes 2. Bi-weekly performance or as needed to support changes. 3. Monthly performance review with identified Client leadership for 30 minutes	1. Governance call 2. Performance review



F. PROJECT TIMETABLE AND MILESTONES:

**Transition timelines will be revalidated and agreed by the parties after the delivery of the process discovery sessions.*

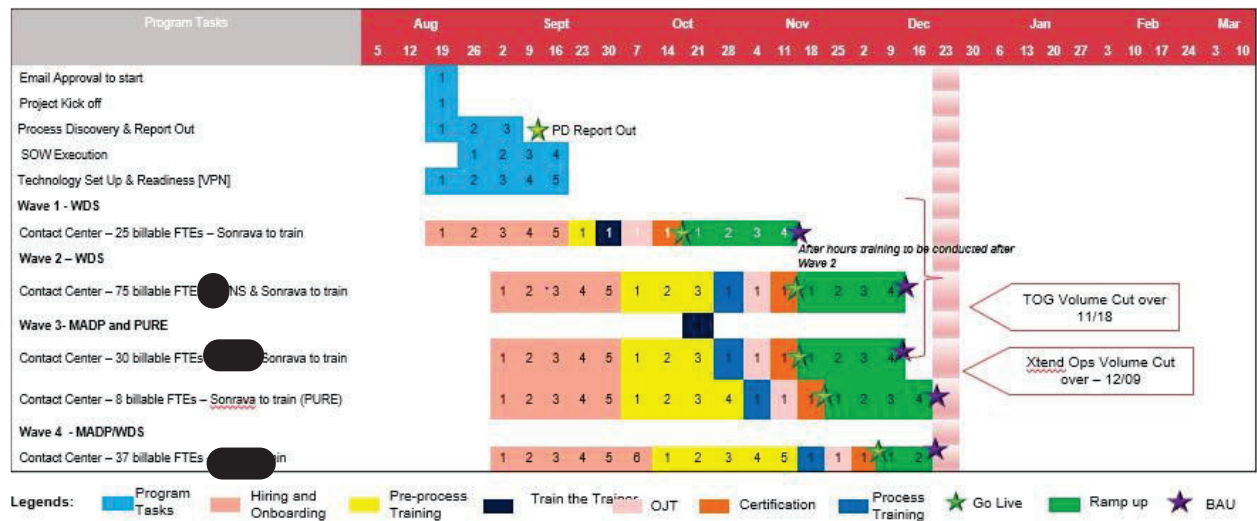

The above transition plan is subject to change basis mutual discussion between the parties and has dependencies listed below:

1. The Client will provide the WDS and MADP volume split between all the existing vendors.
2. The Historical volume for the past 6 Months will be shared with XYZ.
3. The Client trainer's availability to train and support during the ramp-up period from Wave 2, 3 for WDS
4. MADP Client trainers to be available to conduct TTT in Oct for XYZ leaders and support training that would start from Nov 2024.

TRANSITION PHASES

The following table sets out the detailed list of activities during the transition phases:

1. Activity Sequencing

- a) Transition Services are organized into transition waves and transition phases.
- b) The following phases represent the main groupings of XYZs' transition methodology-related activities for each transition wave.
- c) These transition phases will occur in accordance with the timeline outlined in the transition plan:



Transition Phase	Description	Outcome / Deliverable
Engage Phase	a) Create a transition plan b) Create individual workstream plans c) Commence hiring d) Process discovery workshops e) Contracting f) Define success criteria g) Client system and apps inventory h) XYZ & Client communication & escalation plan i) Finalize VOT survey respondents	a) Transition plan and individual workstream plans b) Client system and application inventory c) XYZ and Client communication and escalation plan
Architect Phase	a) Create detailed knowledge transfer plan for new hire b) IT solution design finalization c) Knowledge transfer planning d) Track hiring and onboarding e) Compile task list (at activity level) for in scope processes f) Knowledge transfer readiness review g) Finalize seeding staff list and roll out offers h) Define operational metrics i) Detailed process document creation and final approval by client j) Final list of client SMEs for knowledge transfer j) Client approval on knowledge transfer plan	a) Client approved knowledge transfer plan for new hires b) IT solution design document c) Knowledge transfer readiness checklist operational metrics defined d) Client SME list for knowledge transfer for new hire Client approved process documents
Build Phase	a) XYZ infrastructure set up for Knowledge transfer b) Configure systems / Environments c) Connectivity and performance testing d) Create stabilization plan e) Complete User access creation f) & system profiles g) Create volume ramp up plan h) Conduct toll gate 1	a) Toll gate 1 checklist b) Confirmation of application testing for new hires



Transition Phase	Description	Outcome / Deliverable
	i) (knowledge transfer readiness for new hire)	
Learn Phase	a) Knowledge transfer b) User Acceptance Testing for production c) Establish BAU governance framework d) Finalize volume ramp up plan e) Finalize cutover / stabilization plan f) Finalize performance management plan g) Certification of XYZ's resources h) Conduct toll gate 2 (Go-Live) i) Operational risk identification and mitigation	a) User Acceptance Testing results for production b) BAU Governance Framework finalized Toll gate 2 checklist c) Operational risk mitigation roadmap finalizes cutover / Stabilization Plan d) Finalize Performance Management Plan
Execute Phase	j) Go-Live of processes k) Volume ramp up as per agreed plan l) Monitor volume ramp up m) Performance management tracking - Service level/ metrics performance n) IT performance testing ,performance feedback for XYZ's team / resources o) Handover from transition to operations p) Conduct toll gate 3 (business as usual)	e) Performance management reporting f) Toll gate 3 checklist (handover from transition to operations)

2. Transition Services Implementation Process

- a) XYZ will perform the transition services in a way that ensures continuity of all of the Client’s processes being transitioned.
- b) The Client’s program management office (or its designee) and the XYZ project manager will meet as required by the Client until the transition services are completed to review their status.

3. Transition Services Acceptance

- a) The parties will agree on acceptance criteria for the transition milestones (the milestone acceptance criteria) as per the timeline defined in the project plan.

- b) Upon completion of the transition milestone, XYZ shall submit a written notification to the Client informing the Client that XYZ has completed such transition milestone and that it has satisfied the applicable milestone acceptance criteria.
- c) The Client will use reasonable efforts to review the submission promptly, but in any event within ten (10) business days and determine whether such transition milestone is ready for acceptance.
- d) The Client will use commercially reasonable efforts to review a transition milestone for acceptance and send written notification to XYZ confirming acceptance the completion of the transition milestone or that the transition milestone is not yet ready for acceptance (including the specific areas of non-compliance) within the agreed timeframe.
- e) Thereafter, XYZ shall promptly, but in any event, within four (4) weeks, remediate issues and deficiencies associated with such transition milestone and shall notify Client again upon completion of such effort.
- f) If, after such remediation period, the transition milestone has still not been successfully completed, such transition milestone shall be deemed to have not been met.

4. Transition Services Commencement

- a) Transition services have started on the Effective Date.
- b) The transition services shall be completed within the agreed timelines in the detailed transition plan with adequate support from Client as specified and agreed in the detailed transition plan.

5. XYZ Primary Responsibilities.

XYZ will perform the tasks in accordance with the transition plan. XYZ's responsibilities include the following:

- a) Identify the resources (including equipment, software, and XYZ personnel) that XYZ requires to complete the transition.
- b) As soon as practicable, but no later than fifteen (15) business days after the Effective Date, establishing a transition project management office with sufficient members of XYZ personnel to manage the transition services set out in the transition plan (the "**Transition Team**").
- c) Managing and delivering, where appropriate, the transition services, including the transition plan and the management activities and deliverables set out therein, and overseeing the deliverables in the detailed transition plan.
- d) Identifying the tasks required of both Client and XYZ to complete the transition services, which includes identifying and managing, with the assistance of Client the business and technical issues that may affect the transition services.
- e) Developing and implementing the processes necessary to complete the transition services as set out in the transition plan.
- f) XYZs' responsibilities during the knowledge transfer phase shall include:
 - i. Monitoring and tracking the progress of knowledge transfer against the knowledge transfer plan agreed between the Client and XYZ.
 - ii. Highlight any risks and deviations from the agreed knowledge transfer plan and suggest workaround/ mitigation plans for them.
 - iii. XYZ will onboard the Billable FTEs as agreed upon in the SOW.



- iv. The workstation and IT equipment will be provided as agreed in the IT solution document.
- v. Connectivity to be established for work from office and work from home users.
- vi. Weekly project status reports highlighting key updates milestone, risk.
- vii. Fortnight an executive meeting to be conducted and circulate the key actions and risk for the project.
- viii. Completion of transition Infosec risk assessment as 1-time activity during the transition phase.
- g) Providing and managing weekly detailed transition plan activities and providing updates to Client, which will:
 - i. list activities scheduled during the then-current weekly reporting period.
 - ii. list activities planned for the next weekly reporting period.
 - iii. update the status of changes (cumulative, approved, rejected or implemented).
 - iv. address Client concerns and respond to Client's recommendations.
 - v. provide updates on identified issues.
- h) Conducting tollgate reviews with Client.
- i) Performing latency testing.
- j) Providing internet access during remote work situations only (i.e., work from home).

6. Client Responsibilities.

The Client shall ensure the following:

- a. Establish a Transition Team to support the XYZ and manage Client transition deliverables.
- b. Provide non-confidential information and assistance as reasonably requested relating to XYZ's activities as described in the detailed transition plan.
- c. Participation in process discovery and, in accordance with (b) above, sharing the historical data, materials, IT application list.
- d. Provide any existing process documentation for in-scope activities and personnel. Documentation can include:
 - i. Comprehensive in-scope task list – at activity level (signed off by Client);
 - ii. As-Is and available exception procedures and nuances.
 - iii. Detailed system related documentation for in-scope activities, that can be incorporated into standard operating procedures as part of adapted process documentation.
 - iv. List of all macros, pivot-based reports, and other automation currently deployed across all business units.
- e. In absence of any process documentation and in-scope task / activity list, the parties acknowledge that there will be an open risk on the comprehensive and effectiveness of knowledge transfer which may impact XYZ's transition timelines and deliverables. As a mitigation, both parties agree that the detailed task list will be developed by XYZ within 30 days of knowledge transfer completion. Such a detailed task list will be reviewed and signed off by the Client.



- f. Provide availability of trainer’s resources and quality team to support XYZ during the ramp up.
- g. Provisioning of access on applications, completion of the UAT and troubleshooting on all pending issues for XYZ as per the project plan and reporting access to XYZ support staff.
- h. Access to the Client’s environment in order for the onboarding of XYZs staff in readiness for the start of the Client’s process training.
- i. Agreement and signoff on volume, cut over plan, ramp up plan before Go-Live.
- j. Accreditation to be completed for XYZs’ all staff including the leadership team before start of live transaction.
- k. Raw data to be shared with XYZ for reporting weekly performances during the ramp up period
- l. Ensure backlogs are kept to a minimum during cutover to XYZ. In case of backlogs, the parties will agree to make suitable adjustments to augment XYZ Personnel in accordance with Section 30 of the Agreement ‘Change Control Procedure’
- m. Participation in scheduled governance forums and tollgate milestone events for sign offs.

7. Transition Methodology and Phases

XYZ will manage the transition services using XYZs proprietary transition methodology, named “EnABLE”.

8. Description of Critical Transition Milestones:

Milestone	Acceptance Criteria
Tollgate 1	SOW to be executed by both the parties
	Process discovery report out pack to be signed off by Client. • Finalise the scope at a country level including the nuances. • Validation of to be process maps and gap analysis to be completed. • Agreement on the target operating model and implementation plan. • Shift timings at a country level and XYZ operating model to be agreed. • List of applications to be agreed. • IT solution design document with XYZ site to be signed off by Client; • Detailed project plan jointly agreed and baselined; • Day by day knowledge transfer / training plan agreed and approach to be agreed; • Communication made to the Client’s trainers/SMEs for knowledge transfer; • System accesses for XYZ knowledge transfer resources have been requested/provisioned;



	• Hiring/Staffing of XYZ team completed;
Tollgate 2	SOW for services in scope has been signed off • XYZ infrastructure procurement, installation and facility set-up completed; • IT connectivity to Client applications established and tested; • Training and certification of XYZ resources completed; • Client communication to all impacted internal and external parties completed; • Metric guide (operational definition of performance metrics, targets and reporting structure) agreed with Client; • Cutover / volume transfer plan agreed with Client; • Final BCP document shared with Client; • Transition success criteria agreed during the ramp up period. • Process SOPs for new activities to be created during KT and signed off.
Tollgate 3	Volume ramp-up / intake completed as per agreed cutover / volume transfer plan • Business As Usual governance established; • Operational performance reporting commenced, per agreed metric guide; • Implement agreed BAU operating Governance Framework (Target Operating Model); • Stabilization Support requirement from Client; • Handover from transition to operations complete;

G. WORK PRODUCT STANDARDS:

XYZ agrees to the below service levels post BAU - Go Live *, as described below:

Process Group	SLA (Name)	SLA Description	Operational Definition (As-Is)	Data Source	Target (As is) % *	Measurement Window
Inbound Calling	Conversation Rate	SLA	The percentage of patient inquiries specifically seeking new appointments that are successfully converted into scheduled appointments. Calls for rescheduling, cancellations, or general inquiries will be excluded to provide a true measure of conversion effectiveness	Genesys + BI Report	70%	Monthly



			Formula: Conversion Rate % = New Appointments Scheduled / Total New Appointment Calls X 100 Parameters: - New Appointments Scheduled: Count of patient inquiries for new appointments that result in a confirmed booking. - Total New Appointment Calls: Total number of inbound calls specifically seeking new appointment scheduling, excluding calls for rescheduling, cancellations, or general inquiries.			
Ortho Attach Rate	SLA		The percentage of scheduled appointments where a free orthodontic consultation is successfully upsold. This metric measures the contact center’s effectiveness in promoting orthodontic services during the appointment scheduling process. Formula: Ortho Attach % = Scheduled Appointment with Ortho Upsell / Total Scheduled Appointments X 100 Parameters: - Scheduled Appointments with Ortho Upsell: Total number of appointments that include a free orthodontic consultation. - Total Scheduled Appointments: All scheduled appointments, irrespective of service type.	Genesys + BI Report	30%	Monthly
Service Level	SLA		This relates to what percentage of calls are answered or abandoned within the agreed SL time frame. It is critical to identify the point at which measurement is made, VDN or Split Skill.	Genesys	80% within 20sec	Monthly
			$SVL = \frac{NCH \text{ in } X \text{ seconds}}{NCO \text{ in } X \text{ seconds}}$ $SVL = \frac{(NCH \text{ in } X \text{ seconds} + NCA \text{ in } X \text{ seconds})}{NCO}$			
Quality	SLA		DPO Weightage/Point based Measurement System -	Sonrava QA sheet audited by XYZ QA	95%	Monthly
Average handle Time	KPI		This is the amount of time spent on average for each ACD call. It includes Talk Time, After Call Work, both associated and non-associated, and Hold Time. Time spent on either inbound or outbound calls while in ACW mode is included as ACW Time.	Genesys	350	Monthly
			AHT = ATT + ATOH + ACW			
Calls Per Hour	KPI		This is the total number of inbound calls which were answered by agents after being offered to the split/skill and includes those calls which	Genesys	8	Monthly



			were transferred internally using the split/skill transfer number. The same as ACD calls.			
Inbound Calling	Show Rate	KPI	Tracks the rate at which patients attend scheduled appointments. Recognized as a KPI rather than an SLA, the contact center cannot control patient attendance directly. Follow-up interventions such as reminders and confirmations are managed by Sonrava, not the contact center. Formula: Show Rate % = Attended Appointments / Total Appointments Scheduled X 100 Parameters: - Attended Appointments: Confirmed appointments where patients attended as scheduled. - Total Appointments Scheduled: All appointments booked within the period, including no-shows. Note: All KPI's are tracked for monitoring purposes only and do not constitute a performance SLA. Sonrava manages patient follow-up, reminders, and confirmations independently, and these actions lie outside the contact center's scope. The contact center's role is limited to scheduling, and it has no influence over post-scheduling interventions.	Sonrava team to reconcile monthly via BI reports	60%	Monthly


* SLA/KPI to be baselined post BAU Go-Live for a period of 180 days.

** XYZ FTE will work 1701 hours per annum with 85% utilization.

- **Data Access and Reporting Dependency:** XYZ's ability to accurately report and track SLA performance is dependent on timely and full access to both Genesys telephony data and Sonrava's Business Intelligence (BI) reporting systems. Without consistent access to these integrated data sources, XYZ cannot be held responsible for any reporting delays or inaccuracies. Reliable SLA tracking is contingent upon Sonrava providing the necessary data access, permissions, and support to ensure accurate and complete reporting.
- XYZ will be measured on agreed productivity targets for each function, post completion of the baseline period and Client will be responsible for managing any volume fluctuations at an overall function level.



H. TECHNOLOGY ARCHITECTURE AND ASSUMPTIONS

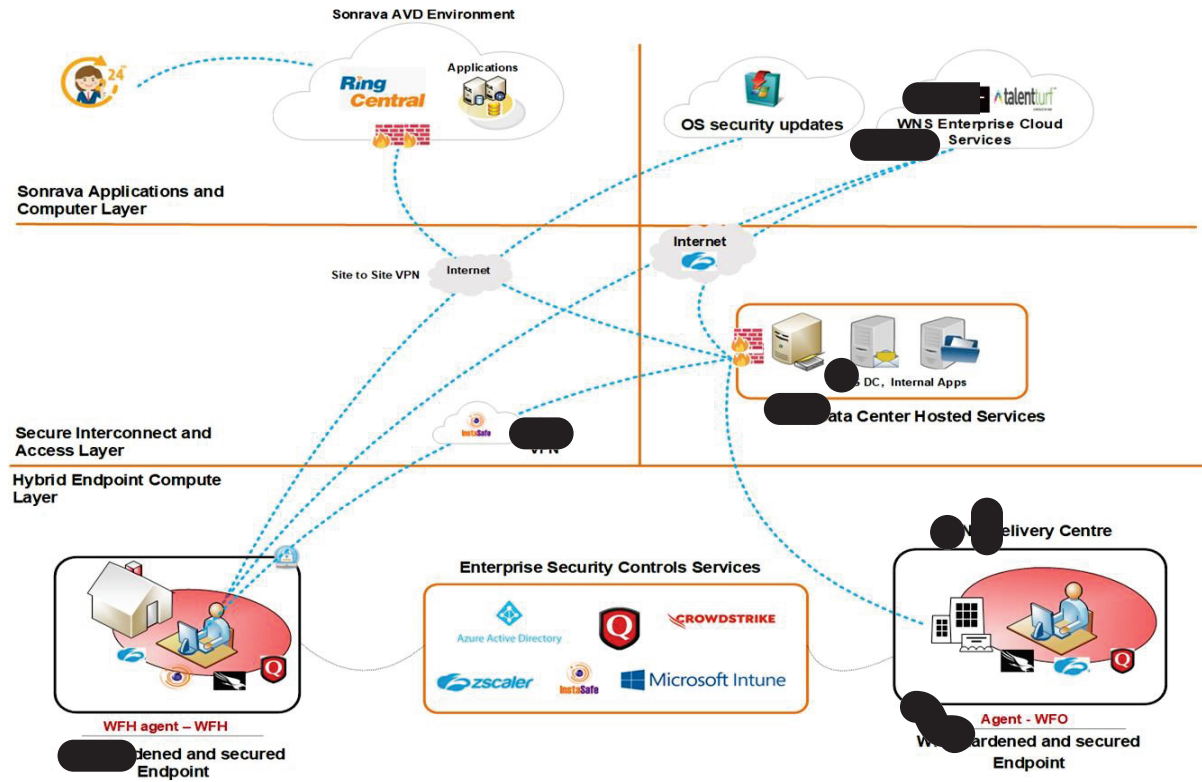

TECHNOLOGY ASSUMPTIONS

- Data connectivity: -
 - Data connectivity over the internet. XYZ will provision internet bandwidth to access Client in scope applications over client provided AVD environment through site-to-site VPN.
 - Internet bandwidth @ 1200 Kbps per user per session considered for accessing the Client applications and voice within Client AVD.
 - The network performance for the Internet connectivity and related parameters such as round-trip Latency, voice quality, Jitter, Packet Loss on Internet services can be provided on "Best Effort Basis".
- Application Access
 - All applications provided by Client within Client AVD and access over internet through site-to-site VPN.
 - Email & MS Office for business requirement wherever required will be provided by Client within Azure AVD.
 - XYZ provided O365 is considered for supervisor as per business requirement for MIS and Reporting purpose.
 - Any other software / hardware required will be charged at additional cost.
 - As part of the proposed solution no Client sensitive data / PII data will be stored and retained within XYZ environment. All data will be accessed within the Client environment and thus all the data will be stored and retain within Client environment only.



- As per DOT (Department of Telecommunications) guideline for XYZ agents in India MS teams should not be connected to PSTN network and calls to landline or mobile will not be enabled.

3. Voice Solution

- Client provided Ring Central Telephony platform will be hosted within Client provided AVD and accessible over internet
- Call and screen recording is not in scope.
- Client will require to provide CDR records as per DOT regulations in India for all the calls that are serviced from XYZ India center. The CDR records are to be retained for a period of 1 year.
- Voice media must not be exposed outside of AVD and traverse directly over internet that will be treated as toll bypass to run voice services over internet from India as per DOT (Department of Telecommunication) regulatory guidelines.
- During the due diligence stage, if it is identified that voice telephony is not accessible within Azure AVD environment, then solution needs to be revisited and MPLS connectivity to be provisioned as per DOT regulation in India. Parties shall mutually agree on the solution and associated commercials as applicable.

4. End User Computing

- XYZ desktop configuration - i3 CPU, 8 GB RAM, 512 SSD, Monitor 22", Windows 10 / 11 OS, Second Monitor 22".

5. Lan Topology

- Secured logical VLAN at XYZ delivery center with restricted inter VLAN communication to XYZ shared services like active directory, end point security, patch management and antivirus update.
- Authentication to the agent desktops through XYZ shared active directory (AD).

6. Technology scope change:

- Any change in scope of business requirement and/or technical design at any stage of the engagement will have an impact on the proposed solution and cost, and the same will be discussed and agreed mutually between the parties through a “Change Order” in accordance with the Change Control Procedure set forth in Section 30 of the Agreement as deemed necessary.

I. **COMMERCIALS:**

- 1 **Billable FTEs Fees** - XYZ will invoice Client monthly by the 5th of the following month, as per the fee structure mentioned below.

- A) **FTE Rates** – FTEs will be billed from Day 1 of process training for hours worked at the rate of \$11.49 per hour. Estimated annual and monthly FTE rates are described in the following table:

Table I: FTE Rates



Location	Role	FTEs	Annual FTE Rate (Year 1)	Monthly FTE Rate (Year 1)
PH - Manila	Agent	175	\$ 24,000	\$ 2,000

The Parties anticipate a total of 175 FTEs on this engagement. Sonrava will be invoiced for the total number of FTE equivalents worked in accordance with the hourly rate specified herein. For clarity, one FTE is equivalent to 2,088 Annual Billable Hours as defined in the assumptions section XYZ shall invoice Sonrava on the actual FTE’s in production during the month on a pro-rate basis.

B) Estimated One-time Training Costs -

175 FTE @80% of the above monthly rate	Estimated training costs of \$193,846
--	---------------------------------------

Sonrava shall be invoiced for training expenses as they are incurred.

C) Technology Costs –

Table I: Tech costs

	Year 1	Year 2	Year 3	Year 4	Year 5
One Time Set-up Charges (Infrastructure) (USD)	\$39,750	--	--	--	--
Annual Recurring Charges (Connectivity) (USD)	\$63,525	\$75,360	\$74,490	\$74,490	\$74,490

Annual Recurring Charges for Connectivity as specified herein shall be invoiced to Sonrava monthly on a pro rata basis.

J. Commercial Assumptions:

S. No.	Assumption	Description
1	Currency	XYZ provided rates and Charges are in USD.
2	Location	The Services will be delivered from Manila, India, delivery centers. Any change in location will impact rates and charges, which shall be agreed upon through a Change Order.
3	General	XYZ charges are based on the scope provided as shared by Client and is subject to due diligence. Any changes to scope, language,



S. No.	Assumption	Description
		location, role-band mix, deal tenure, technology, transition or any other solution variable will result in a suitable adjustment to the commercial proposal.
4	Contract Duration	Pricing is provided for the full 5-year Term, including transition.
5	Inflation	FTE rates stated in Section I (1) (A) (FTE Rates) above, are year-1 rates and will be subject to inflation of @4% per annum applicable on first contract anniversary and every contract anniversary thereafter (including extension/renewal).
6	Payment Terms	XYZ will be paid according to the terms stated under Section 5(Payment) of the Agreement.
8	Taxes	The costs mentioned above exclude taxes (if any), e.g., Sales Tax, VAT, GST, etc. Any applicable taxes shall be charged at the then prevailing rates.
10	Termination	(i)On termination of this SOW, Client shall be liable to pay XYZ all the Charges for the Services performed till the effective termination date.
11	Pass Through Charges	Pass through charges like PSTN, postage, courier, Po Box and specific travel undertaken at customer request, etc. being volume dependent will be recovered on actual. Any T&E associated with the engagement shall be charged additionally on actuals.
12	Transition Cost	Transition cost is based on the current transition plan and any changes to transition plan, timelines, method of knowledge transfer could have an impact on charges. Any charges above and beyond those specified in the Estimated One-Time Trainings Costs section of this SOW shall only be incurred with advance notice to Sonrava and upon mutual agreement between the Parties.
13	Annual Billable Hours	Annual Billable hours include production hours, training hours, meeting & huddle time, holidays, annual leave (including statutory leave) & Tea break but excludes week offs and meal break

K. Holiday Schedule:

Holiday Name	Month	Location
New Years Day	Jan	US
Memorial Day	May	US
Independence Day	Jul	US
Labor Day	Sep	US
Thanksgiving	Nov	US
Christmas	Dec	US



AGREED AND ACKNOWLEDGED

ABC

Signed by:

0378B300EC5741A

Signature



Printed Name

President and C.O.O

Title

14-Nov-2024 | 20:42 EST

XYZ(UK) 

DocuSigned by:

4A0DE4B19CA148B...

Signature



Printed Name

Corporate Senior Vice President - General Counsel

Title


Certificate Of Completion

Envelope Id: 3332AA6B2202470997EFF86F5824EA15		Status: Completed
Subject: ABC_SOW_23-09-2024 from Icertis Inc		
Source Envelope:		
Document Pages: 19	Signatures: 2	Envelope Originator:
Certificate Pages: 5	Initials: 0	
AutoNav: Enabled		
Envelope Stamping: Enabled		
Time Zone: (UTC-05:00) Eastern Time (US & Canada)		
		IP Address: 20.229.43.22

Record Tracking


Status: Original		
11/14/2024 4:49:11 AM		

Signer Events	Signature	Timestamp
---------------	-----------	-----------

	Signed by:  0378B300EC5741A...	Sent: 11/14/2024 4:52:54 AM
		Viewed: 11/14/2024 8:41:23 PM
President and C.O.O		Signed: 11/14/2024 8:42:01 PM
Security Level: Email, Account Authentication (None)	Signature Adoption: Pre-selected Style Using IP Address: 198.90.73.4	

Electronic Record and Signature Disclosure:

Accepted: 11/14/2024 8:41:23 PM
ID: d343cf29-9478-4120-b0e7-2effd966d4d2

	DocuSigned by:  4A0DE4B19CA148B...	Sent: 11/14/2024 8:42:03 PM
		Viewed: 11/15/2024 3:31:09 AM
General Counsel		Signed: 11/15/2024 3:31:15 AM
XYZ Global Service (UK) Limited	Signature Adoption: Pre-selected Style Using IP Address: 85.255.235.6	
Security Level: Email, Account Authentication (None)	Signed using mobile	

Electronic Record and Signature Disclosure:

Accepted: 11/15/2024 3:31:09 AM
ID: 55c199bc-9f75-472a-8b04-1d18b6f463d6

In Person Signer Events	Signature	Timestamp
-------------------------	-----------	-----------

Editor Delivery Events	Status	Timestamp
------------------------	--------	-----------

Agent Delivery Events	Status	Timestamp
-----------------------	--------	-----------

Intermediary Delivery Events	Status	Timestamp
------------------------------	--------	-----------

Certified Delivery Events	Status	Timestamp
---------------------------	--------	-----------

Carbon Copy Events	Status	Timestamp
--------------------	--------	-----------

	COPIED	Sent: 11/14/2024 4:52:55 AM
Security Level: Email, Account Authentication (None)		
Electronic Record and Signature Disclosure:		
Accepted: 11/12/2024 5:18:54 AM		
ID: 55629681-db5a-4f52-9caf-a5b74dbd66f0		

Carbon Copy Events	Status	Timestamp
Security Level: Email, Account Authentication (None) Electronic Record and Signature Disclosure: Not Offered via DocuSign	COPIED	Sent: 11/14/2024 4:52:55 AM Viewed: 11/14/2024 4:28:15 PM
Security Level: Email, Account Authentication (None) Electronic Record and Signature Disclosure: Not Offered via DocuSign	COPIED	Sent: 11/14/2024 4:52:54 AM
Witness Events	Signature	Timestamp
Notary Events	Signature	Timestamp
Envelope Summary Events	Status	Timestamps
Envelope Sent	Hashed/Encrypted	11/14/2024 4:52:55 AM
Certified Delivered	Security Checked	11/15/2024 3:31:09 AM
Signing Complete	Security Checked	11/15/2024 3:31:15 AM
Completed	Security Checked	11/15/2024 3:31:15 AM
Payment Events	Status	Timestamps
Electronic Record and Signature Disclosure		

ELECTRONIC RECORD AND SIGNATURE DISCLOSURE

From time to time, Denali Group, Inc. (we, us or Company) may be required by law to provide to you certain written notices or disclosures. Described below are the terms and conditions for providing to you such notices and disclosures electronically through your DocuSign, Inc. (DocuSign) Express user account. Please read the information below carefully and thoroughly, and if you can access this information electronically to your satisfaction and agree to these terms and conditions, please confirm your agreement by clicking the 'I agree' button at the bottom of this document.

Getting paper copies

At any time, you may request from us a paper copy of any record provided or made available electronically to you by us. For such copies, as long as you are an authorized user of the DocuSign system you will have the ability to download and print any documents we send to you through your DocuSign user account for a limited period of time (usually 30 days) after such documents are first sent to you. After such time, if you wish for us to send you paper copies of any such documents from our office to you, you will be charged a \$0.00 per-page fee. You may request delivery of such paper copies from us by following the procedure described below.

Withdrawing your consent

If you decide to receive notices and disclosures from us electronically, you may at any time change your mind and tell us that thereafter you want to receive required notices and disclosures only in paper format. How you must inform us of your decision to receive future notices and disclosure in paper format and withdraw your consent to receive notices and disclosures electronically is described below.

Consequences of changing your mind

If you elect to receive required notices and disclosures only in paper format, it will slow the speed at which we can complete certain steps in transactions with you and delivering services to you because we will need first to send the required notices or disclosures to you in paper format, and then wait until we receive back from you your acknowledgment of your receipt of such paper notices or disclosures. To indicate to us that you are changing your mind, you must withdraw your consent using the DocuSign 'Withdraw Consent' form on the signing page of your DocuSign account. This will indicate to us that you have withdrawn your consent to receive required notices and disclosures electronically from us and you will no longer be able to use your DocuSign Express user account to receive required notices and consents electronically from us or to sign electronically documents from us.

All notices and disclosures will be sent to you electronically

Unless you tell us otherwise in accordance with the procedures described herein, we will provide electronically to you through your DocuSign user account all required notices, disclosures, authorizations, acknowledgements, and other documents that are required to be provided or made available to you during the course of our relationship with you. To reduce the chance of you inadvertently not receiving any notice or disclosure, we prefer to provide all of the required notices and disclosures to you by the same method and to the same address that you have given us. Thus, you can receive all the disclosures and notices electronically or in paper format through the paper mail delivery system. If you do not agree with this process, please let us know as described below. Please also see the paragraph immediately above that describes the consequences of your electing not to receive delivery of the notices and disclosures electronically from us.

How to contact Denali Group, Inc.:

You may contact us to let us know of your changes as to how we may contact you electronically, to request paper copies of certain information from us, and to withdraw your prior consent to receive notices and disclosures electronically as follows:

To contact us by email send messages to: pnero@denaliusa.com

To advise Denali Group, Inc. of your new e-mail address

To let us know of a change in your e-mail address where we should send notices and disclosures electronically to you, you must send an email message to us at pnero@denaliusa.com and in the body of such request you must state: your previous e-mail address, your new e-mail address. We do not require any other information from you to change your email address..

In addition, you must notify DocuSign, Inc to arrange for your new email address to be reflected in your DocuSign account by following the process for changing e-mail in DocuSign.

To request paper copies from Denali Group, Inc.

To request delivery from us of paper copies of the notices and disclosures previously provided by us to you electronically, you must send us an e-mail to pnero@denaliusa.com and in the body of such request you must state your e-mail address, full name, US Postal address, and telephone number. We will bill you for any fees at that time, if any.

To withdraw your consent with Denali Group, Inc.

To inform us that you no longer want to receive future notices and disclosures in electronic format you may:

- i. decline to sign a document from within your DocuSign account, and on the subsequent page, select the check-box indicating you wish to withdraw your consent, or you may;
- ii. send us an e-mail to pnero@denaliusa.com and in the body of such request you must state your e-mail, full name, IS Postal Address, telephone number, and account number. We do not need any other information from you to withdraw consent.. The consequences of your withdrawing consent for online documents will be that transactions may take a longer time to process..

Required hardware and software

Operating Systems:	Windows2000? or WindowsXP?
Browsers (for SENDERS):	Internet Explorer 6.0? or above
Browsers (for SIGNERS):	Internet Explorer 6.0?, Mozilla FireFox 1.0, NetScape 7.2 (or above)
Email:	Access to a valid email account
Screen Resolution:	800 x 600 minimum
Enabled Security Settings:	• Allow per session cookies • Users accessing the internet behind a Proxy Server must enable HTTP 1.1 settings via proxy connection

****** These minimum requirements are subject to change. If these requirements change, we will provide you with an email message at the email address we have on file for you at that time providing you with the revised hardware and software requirements, at which time you will have the right to withdraw your consent.

Acknowledging your access and consent to receive materials electronically

To confirm to us that you can access this information electronically, which will be similar to other electronic notices and disclosures that we will provide to you, please verify that you were able to read this electronic disclosure and that you also were able to print on paper or electronically save this page for your future reference and access or that you were able to e-mail this disclosure and consent to an address where you will be able to print on paper or save it for your future reference and access. Further, if you consent to receiving notices and disclosures exclusively in electronic format on the terms and conditions described above, please let us know by clicking the 'I agree' button below.

By checking the 'I Agree' box, I confirm that:

- I can access and read this Electronic CONSENT TO ELECTRONIC RECEIPT OF ELECTRONIC RECORD AND SIGNATURE DISCLOSURES document; and
- I can print on paper the disclosure or save or send the disclosure to a place where I can print it, for future reference and access; and
- Until or unless I notify Denali Group, Inc. as described above, I consent to receive from exclusively through electronic means all notices, disclosures, authorizations, acknowledgements, and other documents that are required to be provided or made available to me by Denali Group, Inc. during the course of my relationship with you.
